



GLOBAL
INSPIRA


GLOBAL INSPIRA,
HINJEWADI PUNE



GLOBAL INSPIRA MILESTONE



MILESTONE

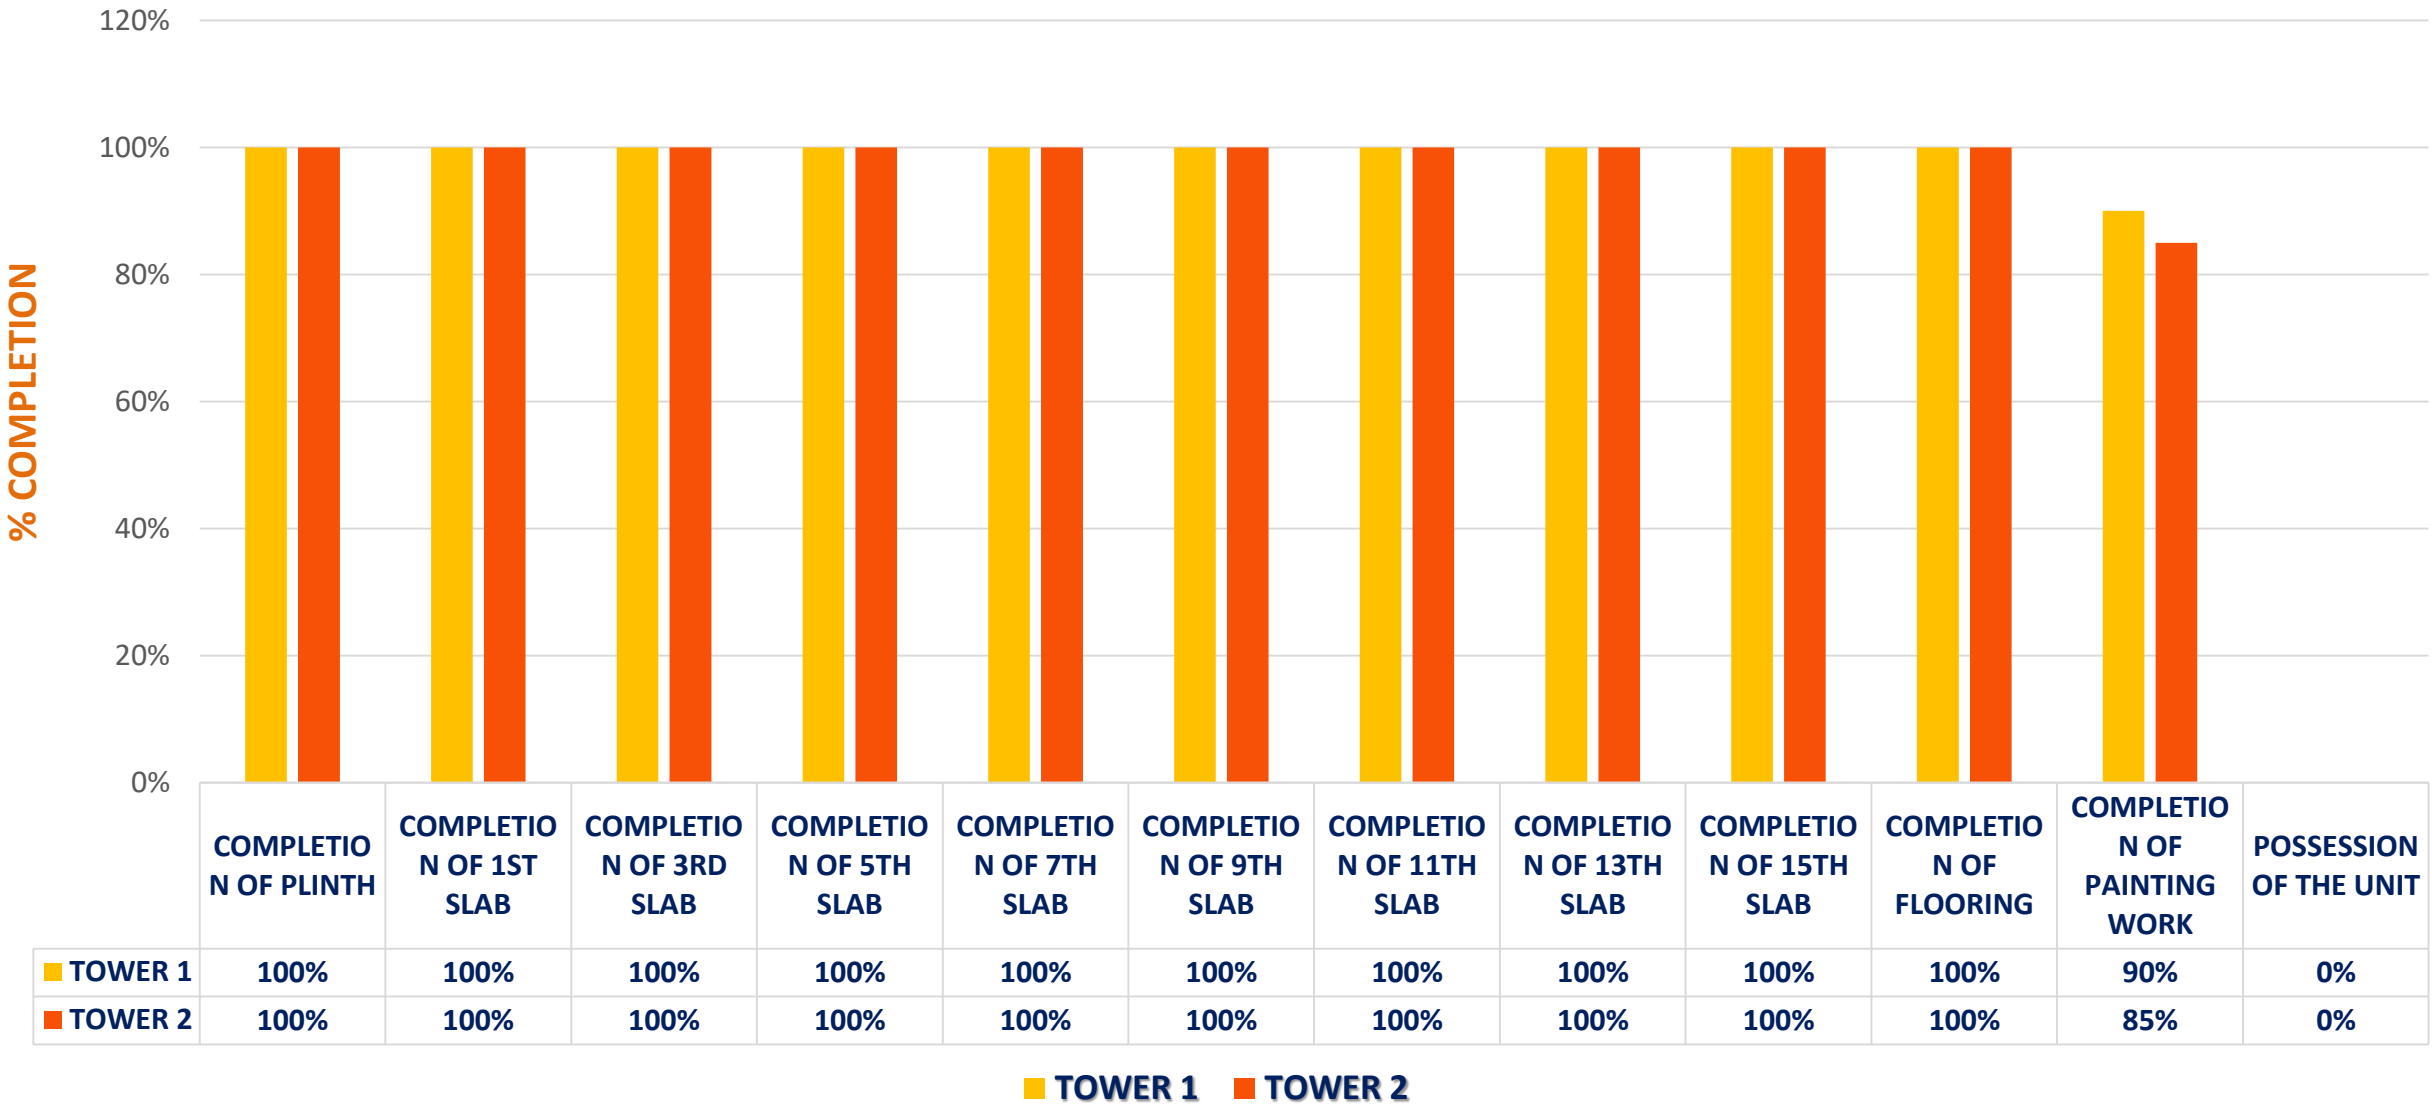

Current status – Global Inspira ph-1

CONSTRUCTION WORK STATUS REPORT



TOWER- 1

- **Excavation** work completed.
- **RCC** work Completed.
- **Internal Electrical** wall and ceiling concealed work completed.
- **Gypsum** work up to 22nd floor Completed .
- **Ceiling Putty** work up to 21st floor completed & **Wall Putty** work up to 21st floor completed & 22nd WIP **Internal paint** up to 20th floor completed
- **Kitchen Platform MS Fabrication work** & **Passage MS Railing work** up to 22nd floor completed.
- **Internal Fire Fighting** work up to 22nd floor completed.
- **Waterproofing** work of Toilet, Attached Terrace & Utility Up to 22nd floor completed.
- **Pex Plumbing** and **slung piping** of Toilet work 22nd floor completed.
- **Kitchen Platform with dado** up to 22nd floor completed.
- **Flat flooring(Tiling)** work up to 22nd floor completed.
- **Toilet dado work Up to** 22nd floor completed.
- **Passage, lift cladding** Up to 22nd floor completed & **Staircase flooring** work completed.
- **Aluminum window frame** work up to 22nd Floor completed, **kitchen window frame** up to 22nd floor completed & , **A. Terrace frame** up to 22nd floor completed.
- **Glass Railing** work of attached terrace up to 11th floor completed 12th to 18th floor WIP.
- **Door Frame & Shutter** frame fixing work up to 22nd floor work completed. **Door shutter** up to 22nd floor completed.
- **Electrical wiring** work up to 22nd floor completed , **Switch plate** 17th floor Completed.
- **Plumbing Down take** of Attach Terrace Plumbing & Utility up to 22nd floor completed.
- **Acid wash** up to 15th floor completed, **Grouting** up to 3rd 13th 14th floor completed 4th 5th 15th floor WIP

Current status – Global Inspira ph-1

CONSTRUCTION WORK STATUS REPORT



TOWER-2

- **Excavation, Footing & Plinth work** work completed.
- **RCC** work Completed.
- **Internal Electrical** wall and Ceiling concealed work up to 22nd floor completed **Gypsum** Work Up to 22nd floor Completed.
- **Ceiling Putty** Work Up to 21th floor Completed & **Wall Putty-** up to 19th floor completed & 20th floor WIP. **Internal paint** up to 19th floor complete & 20th floor WIP.
- **Kitchen MS Platform** Work Up to 22nd Floor Completed . **Passage MS Railing** up to 22nd floor Completed.
- **Internal Fire Fighting** Work up to 22nd Floor Completed.
- **Waterproofing** work of Toilet, Attached Terrace & Utility Up to 22nd floor completed.
- **Pex Plumbing & Slung Piping** Work of Toilet 22nd floor completed.
- **Plumbing Down take** of Attach Terrace & Utility up to 22nd Floor Completed.
- **Kitchen Platform with Dado** up to 22nd Floor Completed.
- **Flat Flooring** Work Up to 22nd Floor Completed.
- **Toilet Dado** Work to 22nd Floor Completed.
- **Passage, lift cladding** Up to 22nd floor completed & **Staircase flooring : fire staircase** up to 22nd floor completed & **common staircase** up to 22nd floor completed
- **Door Frame & fixing** work up to 22nd floor work completed. **Door shutter** up to 19th floor work completed & 20th 21st & 22nd floor WIP.
- **Electrical wiring & switch Plate** work up to 21st floor completed & 22nd floor WIP , **Switch plate** up to 17th floor Completed.
- **Aluminum window frame** work up to 22nd Floor completed, **kitchen window frame** up to 22nd floor completed , **A.Terrace frame** up to 22nd floor completed.
- **Acid wash** up to 15th floor completed, **Grouting** up to 5th floor completed 6th floor WIP


Current status – Global Inspira ph-1



DEVELOPMENT

- **Entrance Gate** slab casting completed & plastering completed & Slab top waterproofing completed **RCC** work Completed.
- **Security cabin RCC** work completed & plastering completed. .
- **STP Blockwork & Plaster** completed.
- **East Side Compound wall** RCC completed.
- **North Side Compound wall** RCC work In Completed.
- **STP & Pump room RCC** work Completed and **Chemical** waterproofing completed & pump installation completed.
- **UGWT & Pump room** RCC Work Completed and **Waterproofing** completed.
- **Swimming pool** Balancing tank, main pool, kids pool casting completed & waterproofing & plumbing completed.
- **Clubhouse** 1st Floor & 2nd slab casting completed ,plastering work completed, wall gypsum & false ceiling completed , outer texture completed
- **Transformer** Civil work completed and texture completed & Internal 1st coat paint completed.
- **Landscape west side** planter wall & murum filling WIP.
- **Amphi Theatre** : Wall casting completed & back filling completed.
- **East side seating** : planter casting WIP & back filling WIP.
- **OWC** : Machine Installation done & fabrication completed & block work completed.



T-1RCC WORK

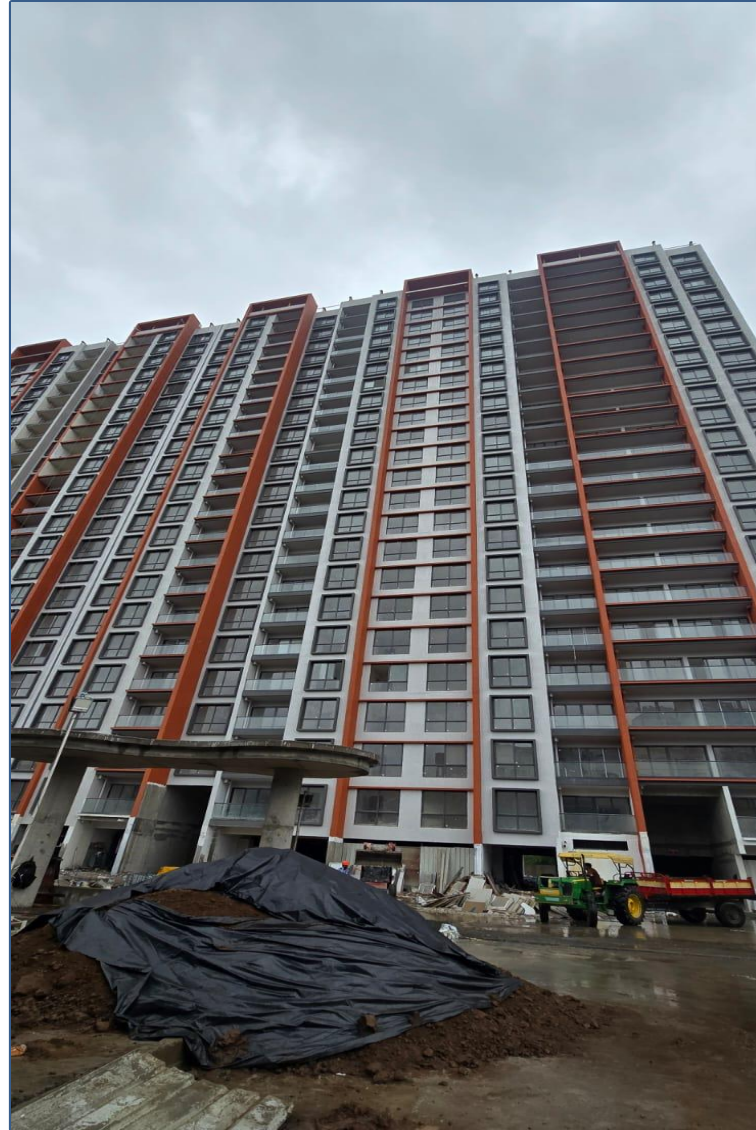



T-1 TERRACE FLOOR




T-1 FINISHING WORK

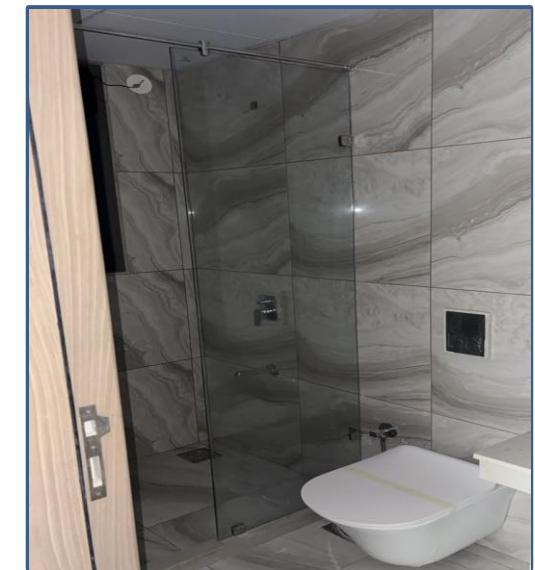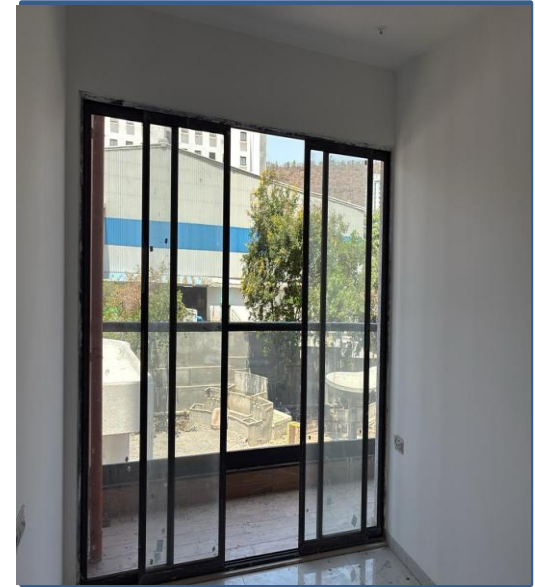

T-1 FINISHING WORK

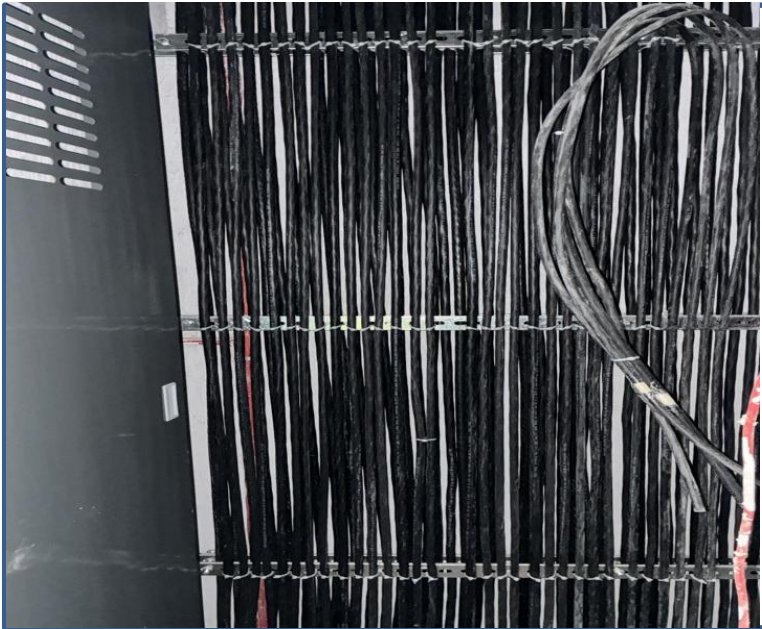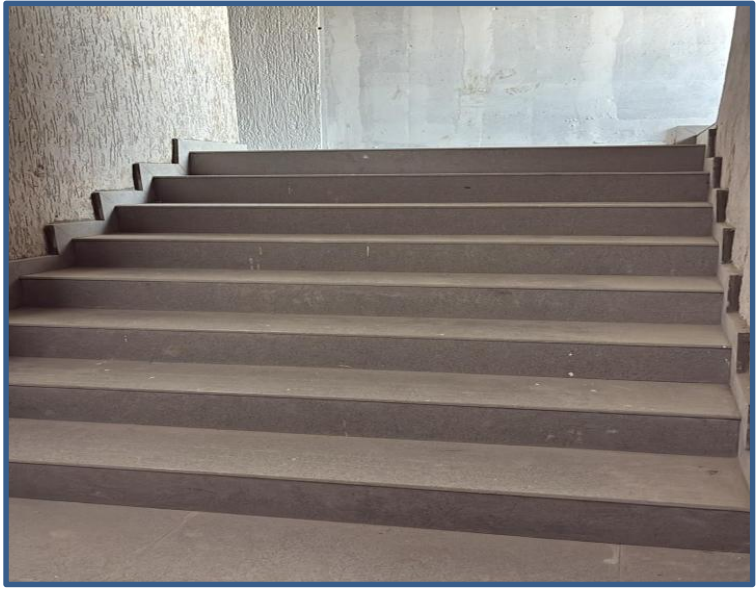

T-2 RCC WORK

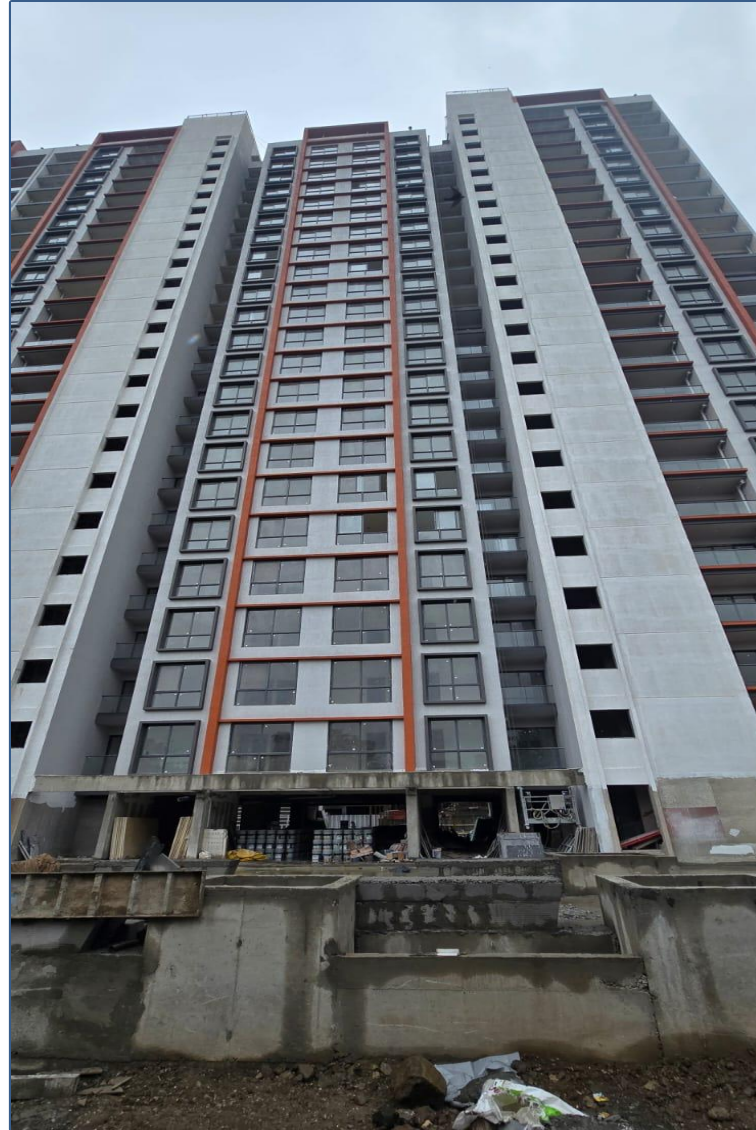

T-2 TERRACE FLOOR



T-2 FINISHING WORK



T-2 FINISHING WORK



Development work

CLUB HOUSE



SWIMMING POOL (BALANCING TANK)



OWC & RAMP



STP



TRANSFORMER ROOM



ENTRANCE AVENUE



DEVELOPMENT WORK

FAMILY NICHE WITH BOUGAINVILLEA




TREE STRUCTURE (NEAR BUS STOP)



Parent & Elderly sitting



WEST SIDE HARDSCAPE

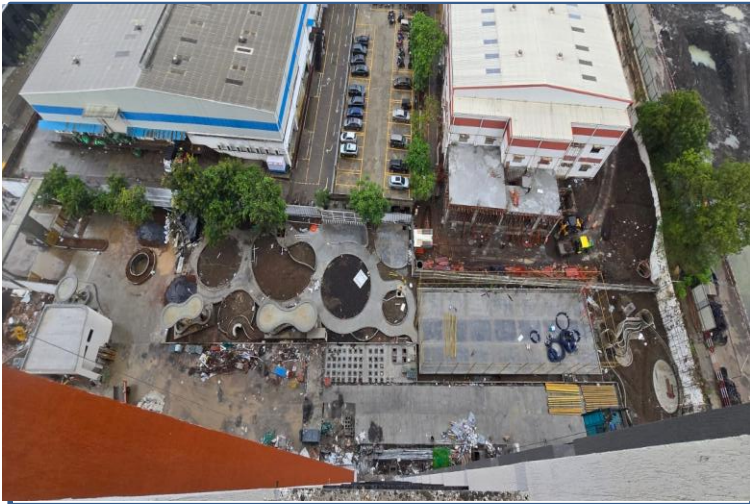

AMPHI THEATER



EAST SIDE SEATING AREA



DEVELOPMENT WORK

UGWT FIRE TANK 1




UGWT DRENCHER TANK



UGWT FIRE TANK 2




PUMP ROOM

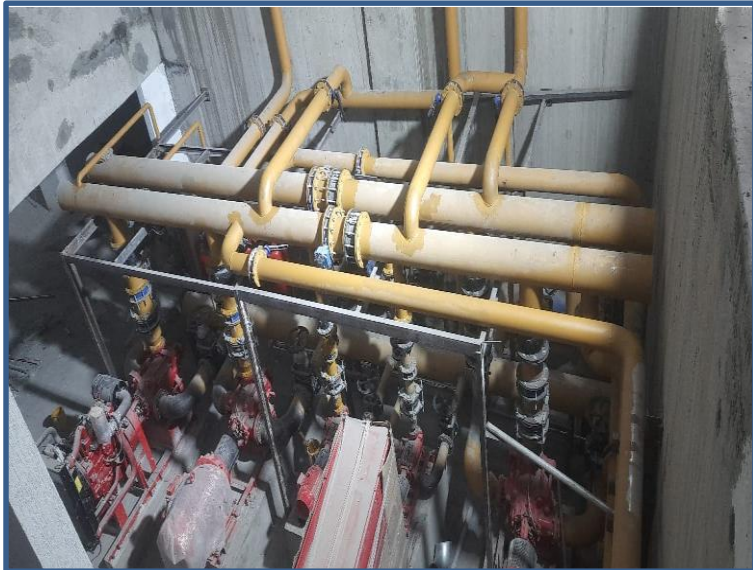

BASEMENT 2 TRIMIX



BASEMENT- 1

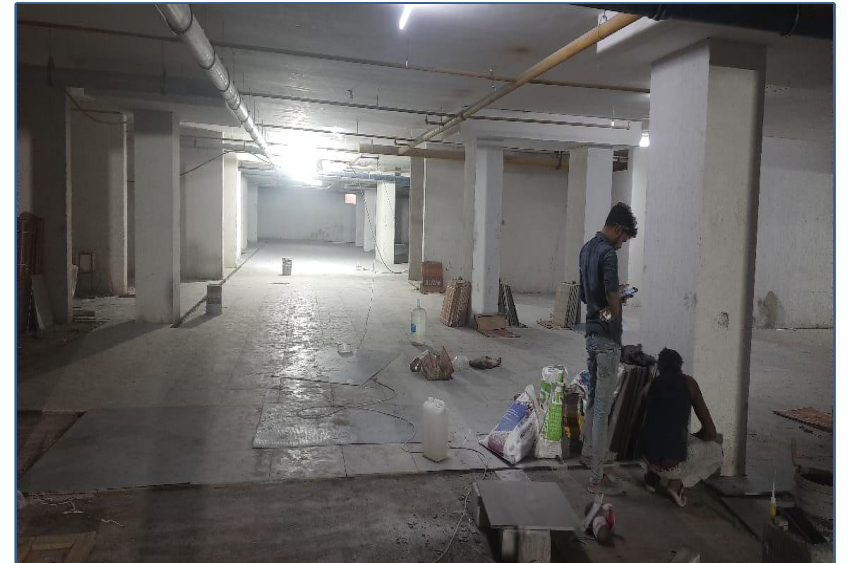

A close-up photograph of two hands shaking in a firm grip, symbolizing agreement or partnership. The hand on the left is wearing a dark blue suit sleeve, and the hand on the right is wearing a light blue and white striped shirt sleeve. The background is a solid light blue color.

Thank You!
